



Professional Diploma in

Project Management

Project Initiation Phase



**Did you
know?**

**The International
Space Station is
one of the world's
megaprojects.**





Objectives

Lesson 2

Identify scope <

Explain feasibility studies <

Identify stakeholders <

Create a project charter <

Initiation phase objectives



Scope

Goals/Deliverables

Feasibility

Stakeholders





Project scope




Scope

- Detailed account of every aspect of the project
- Determine boundaries
- Use visuals
- Be specific




Six phases of defining the scope

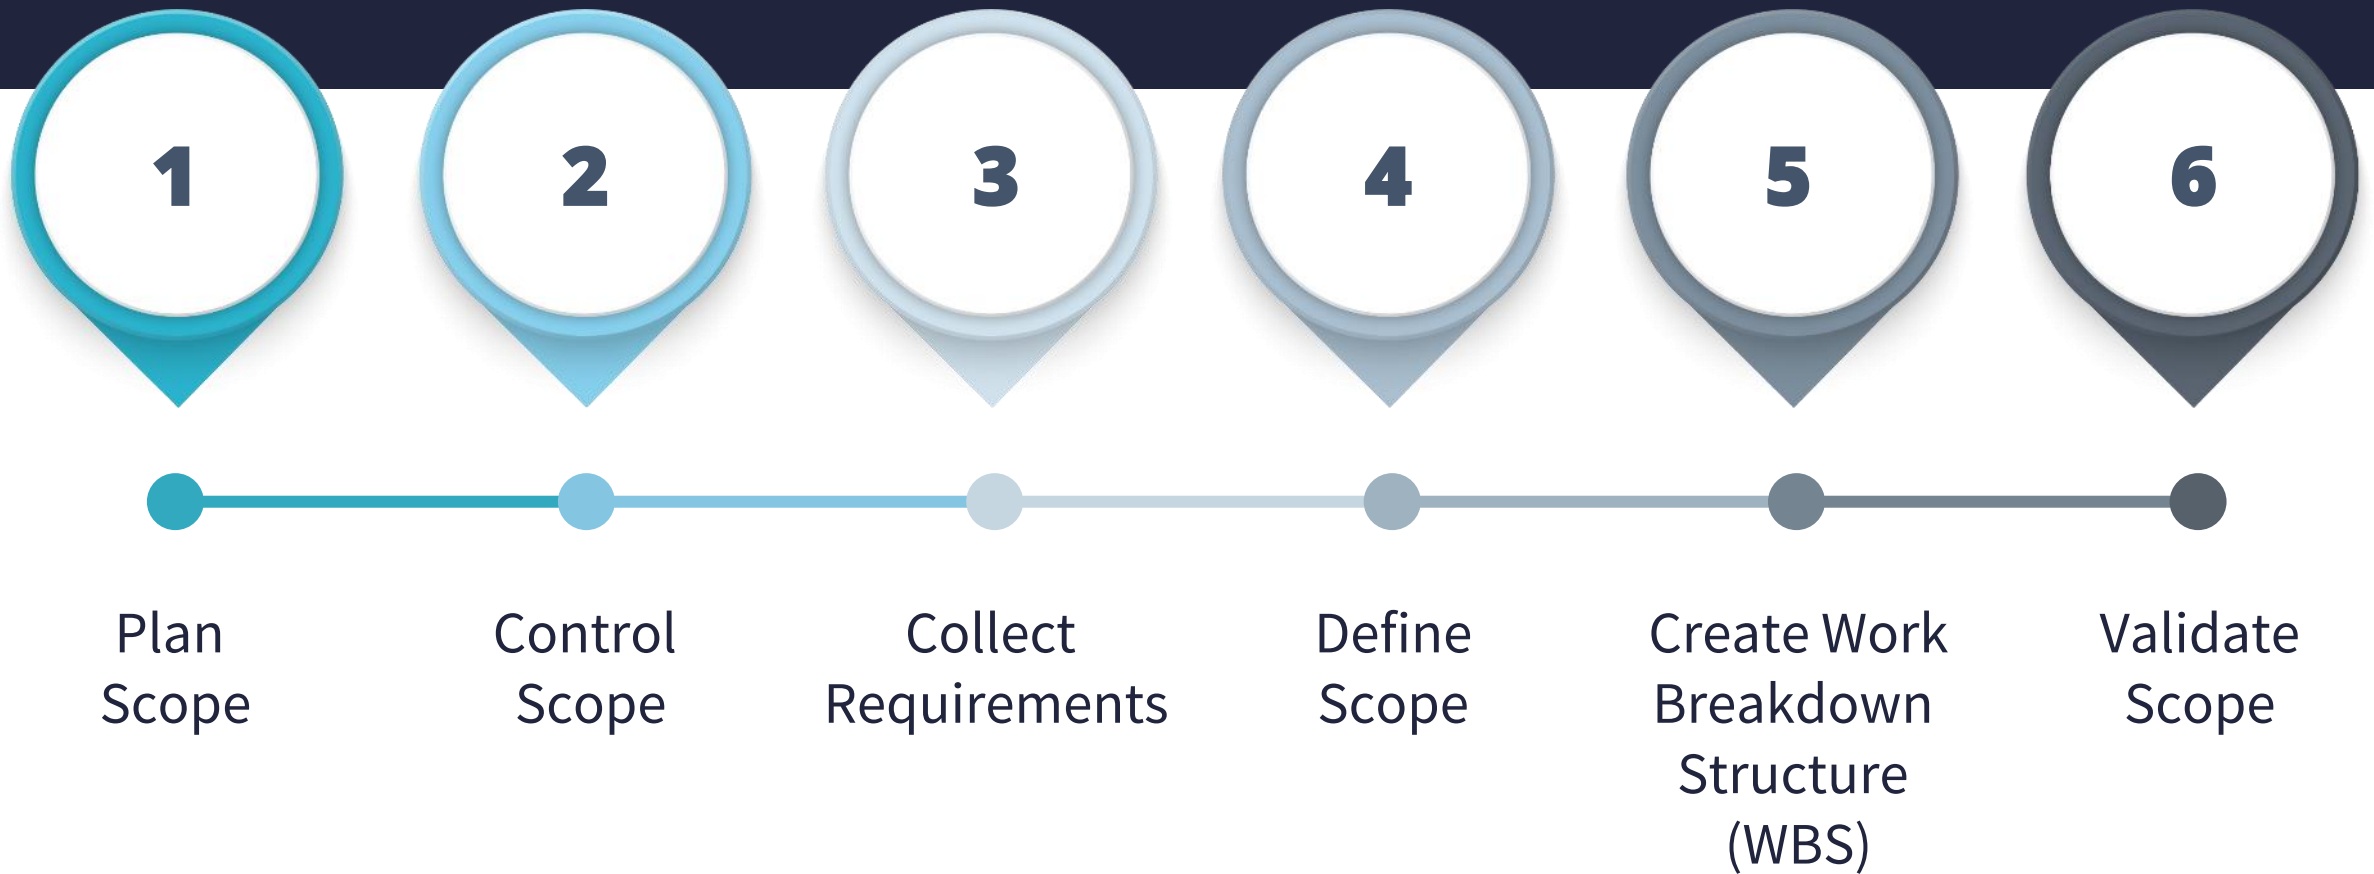



Scope of work sections



Timeline


Deliverables

Milestones

Reports



Scope of work sections



Timeline


Deliverables

Milestones

Reports



Scope of work sections



Timeline


Deliverables

Milestones

Reports



Scope of work sections



Timeline

Deliverables

Milestones


Reports

Scope creep

- Top cause of project failure
- Generally occurs when:
 - Projects are not accurately defined
 - Documents are inaccurate
 - Control is lost/loosely managed



Scope creep

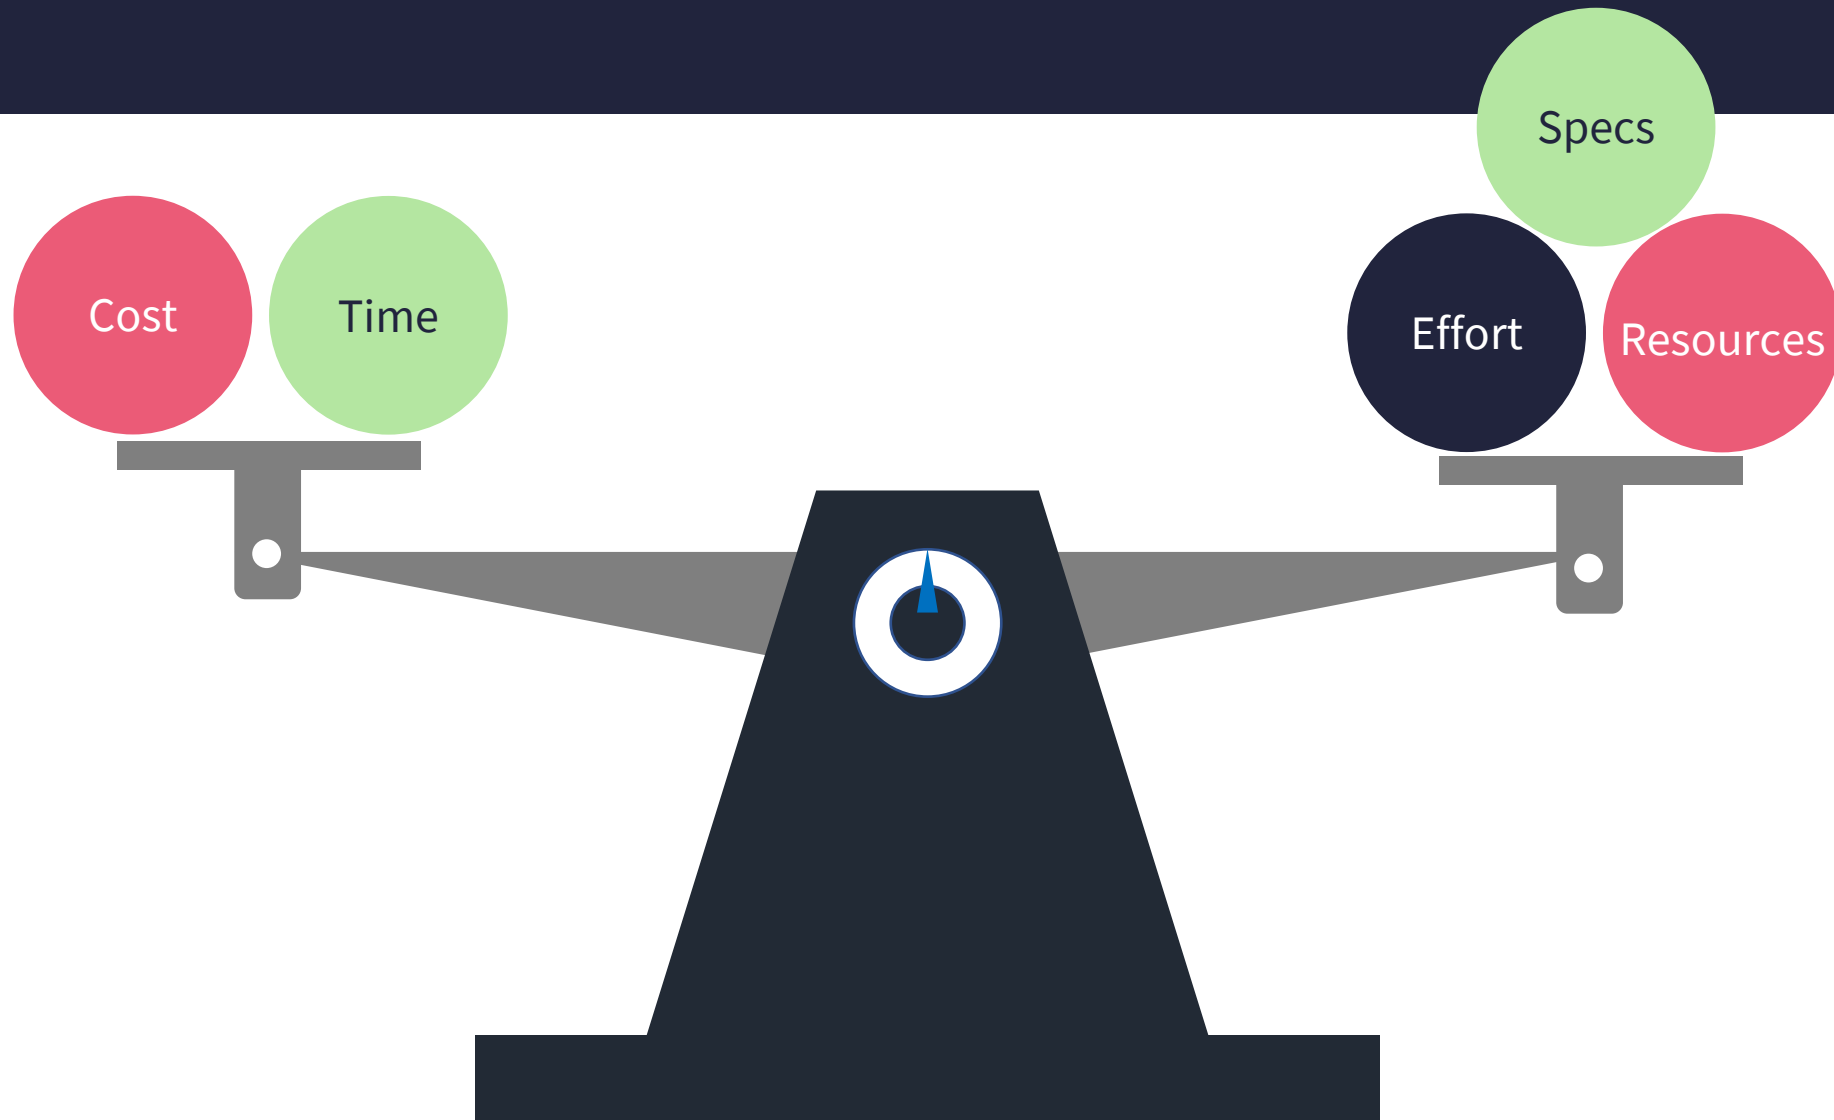



Identifying project goals

- Purpose of undertaking the project
- Long-term outcome
- Tangible statements
- Measurable targets



SMART goals





Identifying project objectives

- What needs to be achieved to reach the project goal
- Five categories:
 - Business Objectives
 - Financial Objectives
 - Regulatory Objectives
 - Effectiveness Objectives
 - Performance Objectives

- 






Identifying milestones

- Sequence in which the project must be completed
- Ensure vital processes are accomplished within the allotted time frame
- Progression is monitored as it moves through each phase



Project feasibility



A feasibility study is an analysis that takes all of a project's relevant factors into account to ascertain the likelihood of completing the project successfully.



A feasibility study

- The project
- When implemented
- Reasons for taking on the project
- Plan to achieve goals
- Best practices
- Report on likelihood of success





Types of Feasibility Studies

T echnical

E conomic

L egal

O perational

S cheduling



Technical Feasibility Study

Technology

Labour

Transport/Shipping

Physical location

Materials



Economic Feasibility Study

Target market

Competitors

Predicted expenses

Demand forecasts
& projections



Legal Feasibility Study

Confirm legal
requirements & restrictions

Copyrights

Permits



Operational Feasibility Study

Compatibility with
business operations

Environment

Ease of operation

Fit for purpose




Scheduling Feasibility Study

Project timeline

Milestones





T.E.L.O.S.

If it is feasible




Red, Amber & Green review (RAG)



Problems are arising that may jeopardise the success of the project

Potential problems have appeared & intervention may be necessary as the project progresses

Project is proceeding as planned & on schedule





Go/No-Go Review

-  **T**echnical Review
-  **E**conomic Review
-  **L**egal Review
-  **O**perational Review
-  **S**cheduling Review





Project stakeholders



Project stakeholder

‘an individual, group or organisation that is **actively involved** in the project’

Identifying stakeholders



**Who is affected
positively or negatively
by the project?**

**Who has the power
to make it succeed
or fail?**

**Who has influence over
other stakeholders?**



**Who makes the
decisions about
money?**

**Who has the potential
to solve problems
with the project?**

**Who has specialist
skills which are
crucial to the project?**

**Who is the
end user?**

**Who is in charge of
assigning or procuring
resources or facilities?**





Internal stakeholders

Top management

Resourcing directors


Finance department

Other teams



Expanded stakeholders


- Suppliers
- Vendors/contractors/subcontractors
- Customers
- Manufacturers
- Environmental organisations
- Community members
- Government
- Media

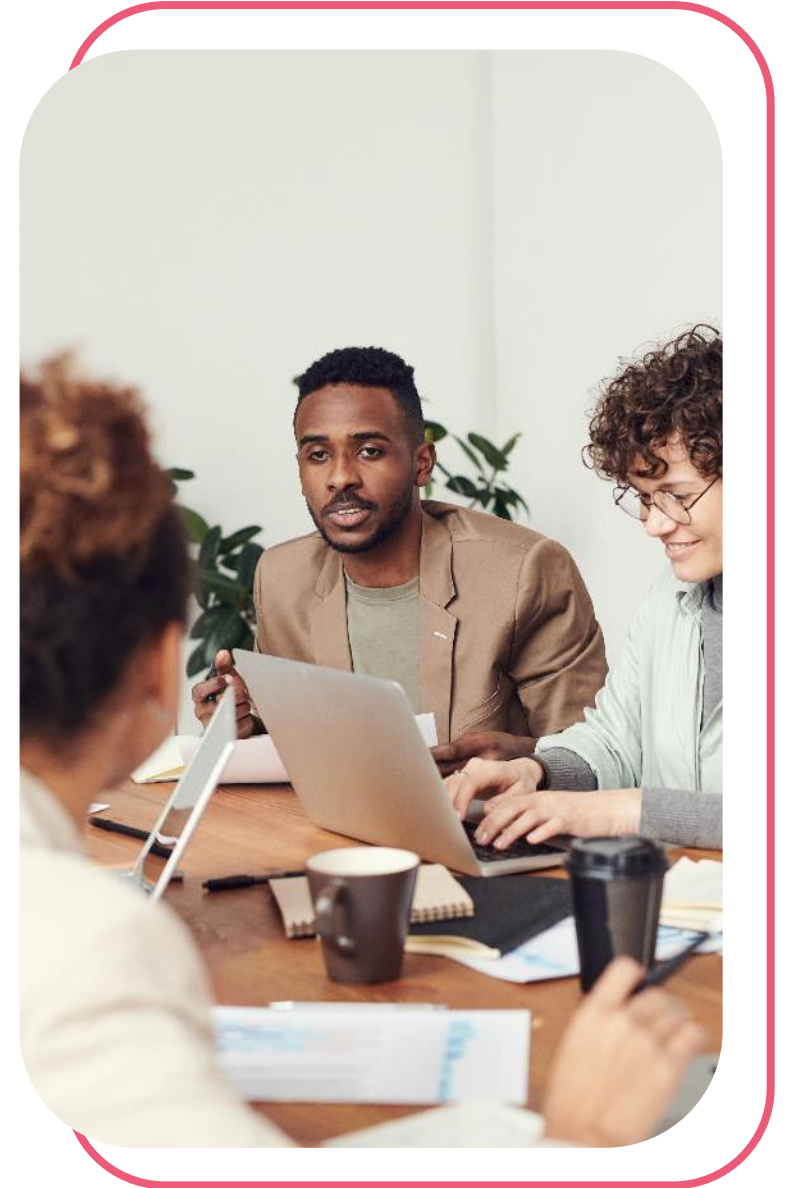

Assessing stakeholder interest & influence




Mapping the power interest matrix

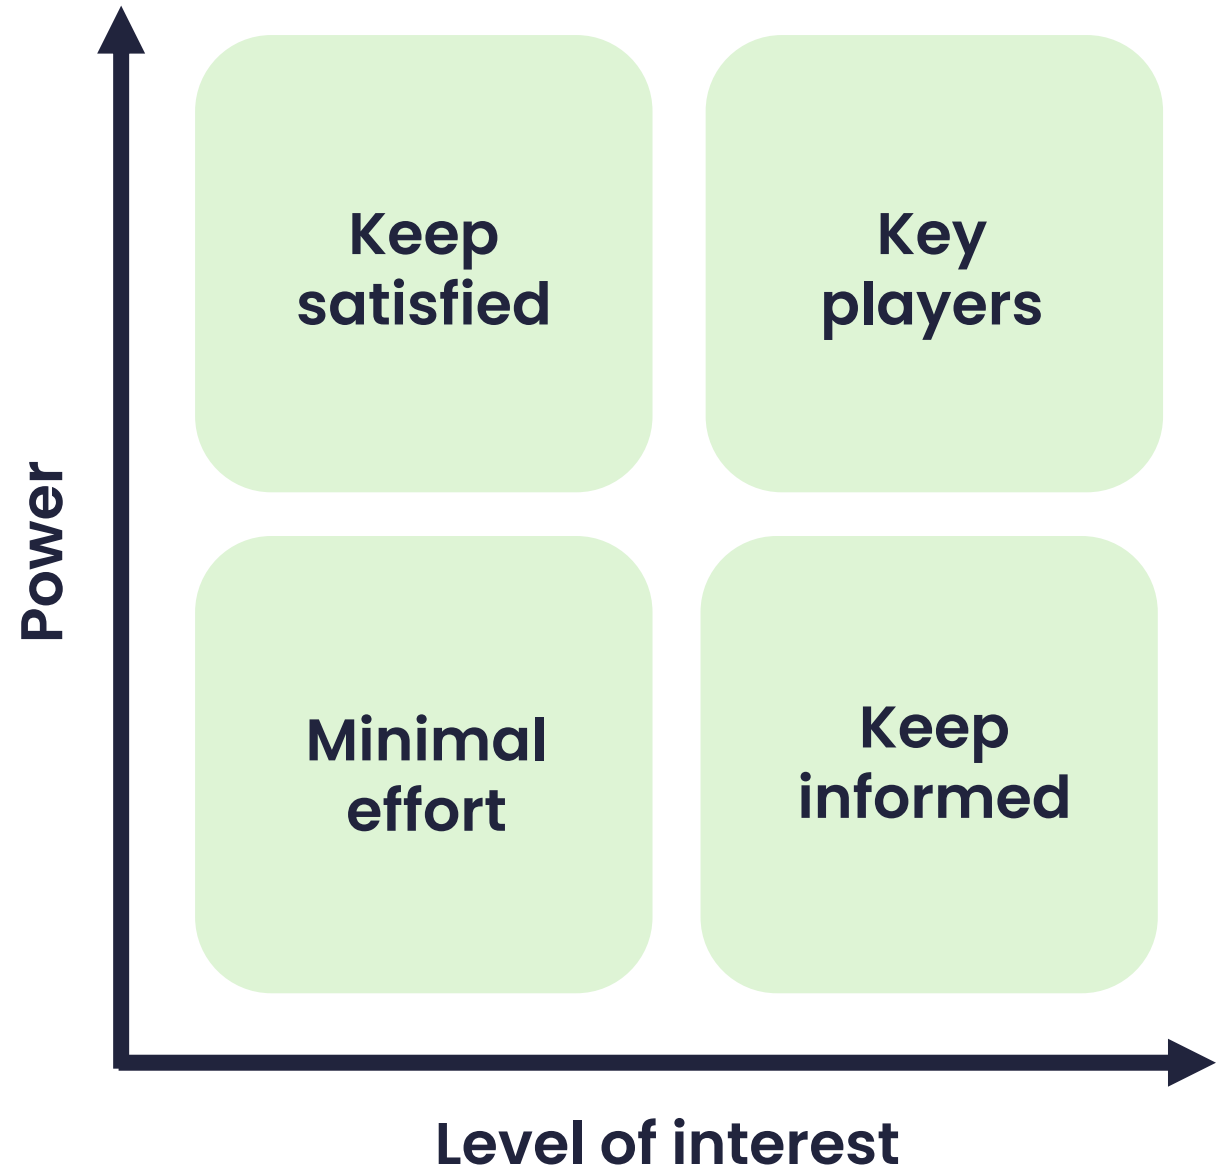


High power & high interest

- Key players
- Need to be engaged regularly and managed closely
- Will require the most effort to keep satisfied

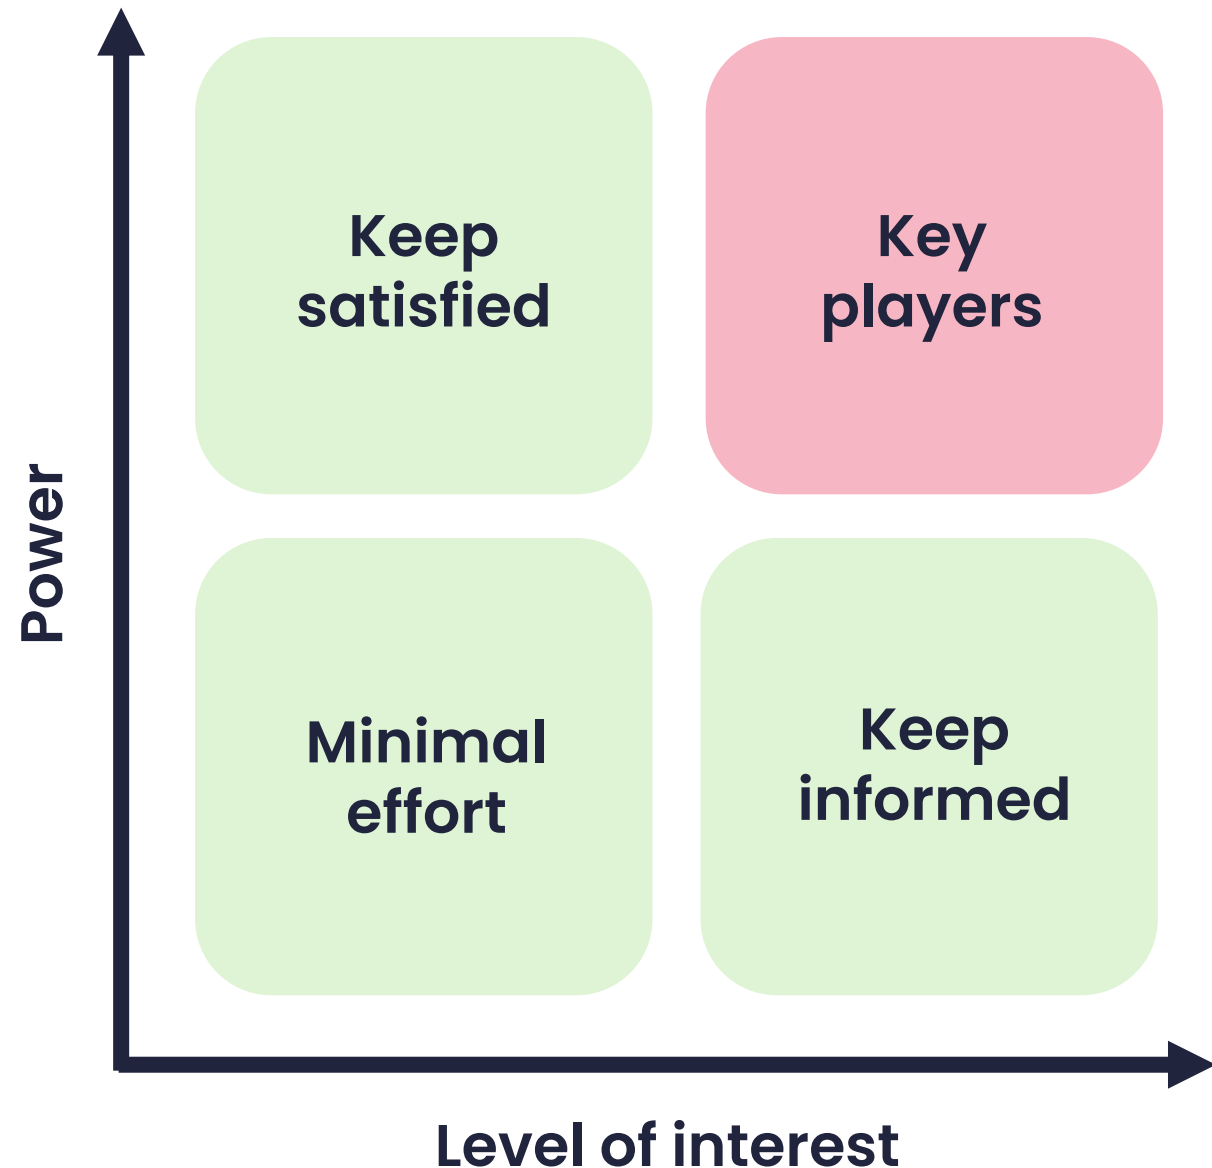


High power & low interest

- Keep satisfied
- Strike a balance between keeping them informed but not overloading them
- Treat with caution

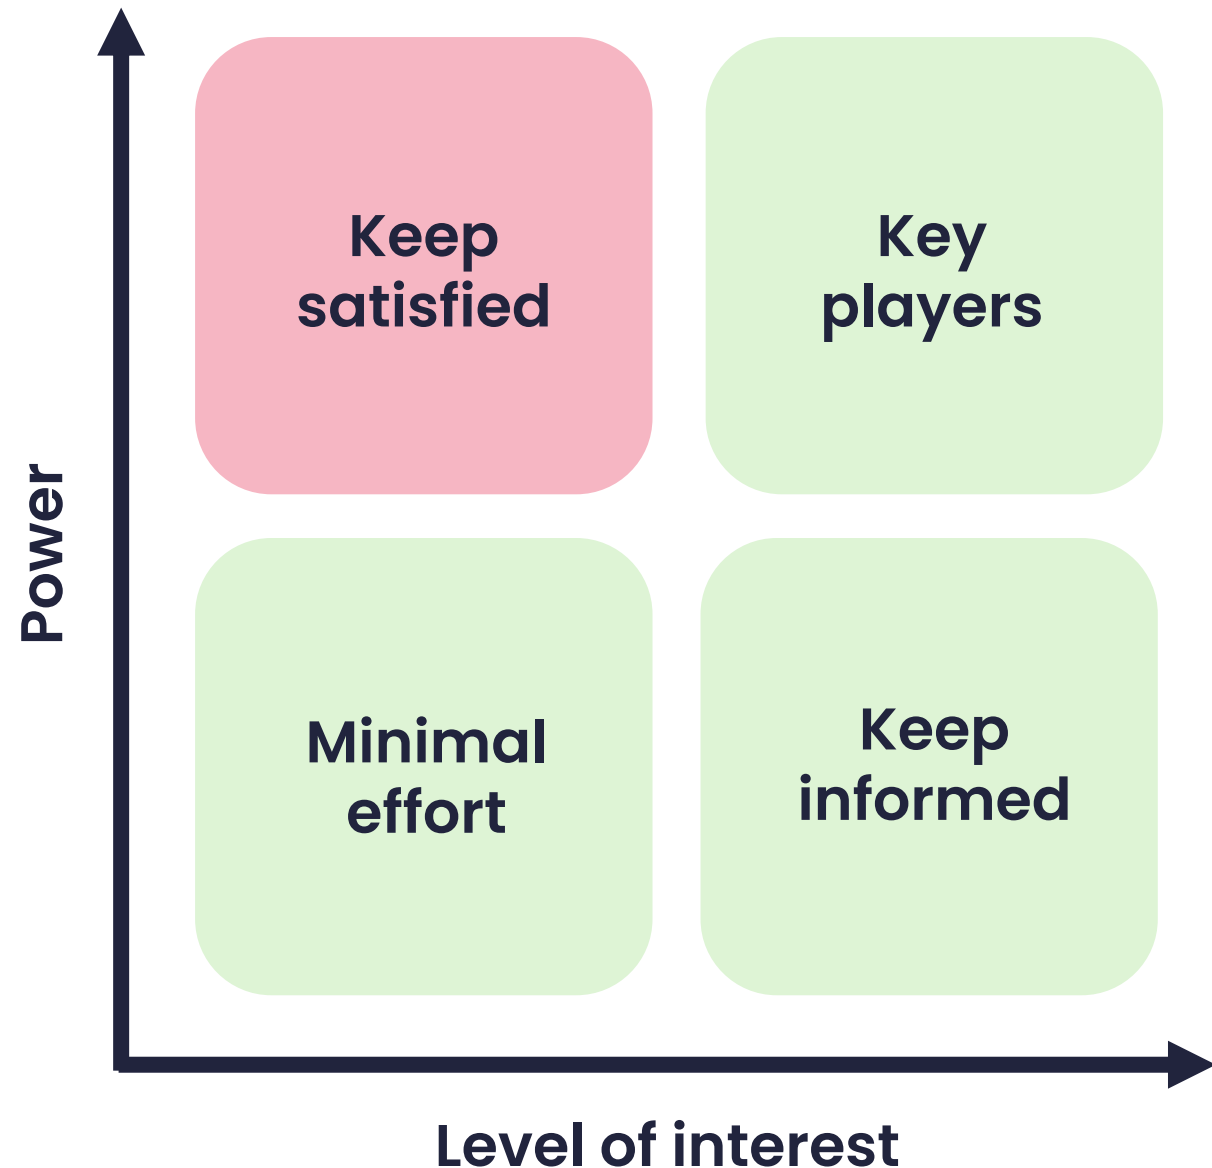


Low power & high interest

- Keep informed
- Make sure they don't have any major issues
- Can be helpful

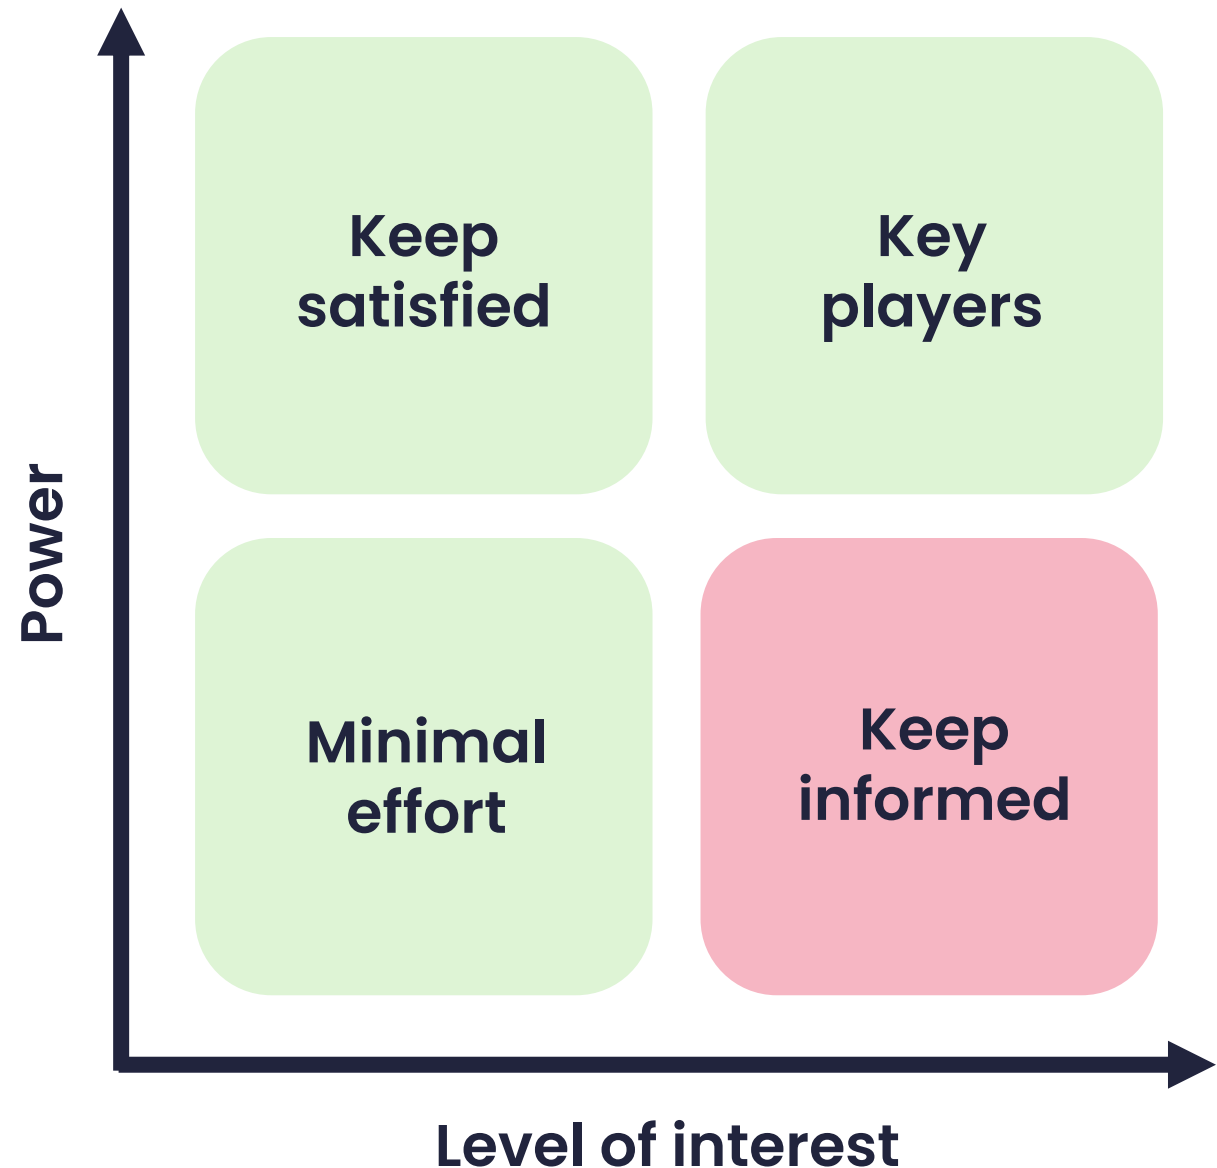

Low power & low interest

- Require minimal effort
- Monitor them but don't bore them
- May become more powerful

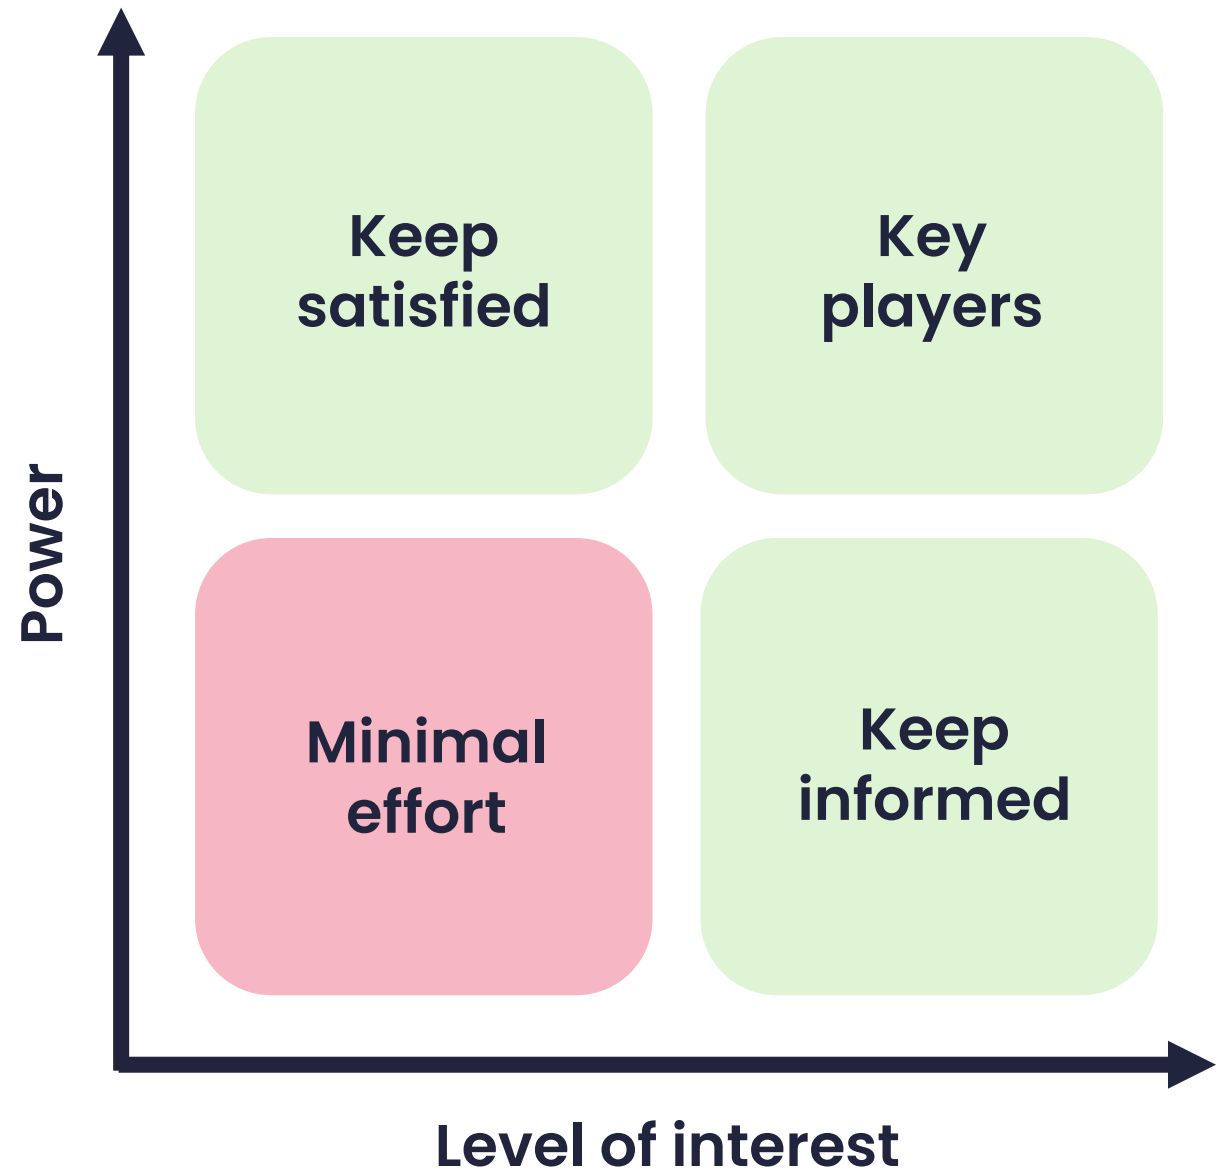

Creating a stakeholder register





Items to include in stakeholder register



Name/contact details


Power

Title/position

Requirements/contribution


Level of interest

Expectations/concerns



Stakeholder register example

Name	Internal/ External	Position	Interest	Influence	Contribution	Concerns	Contact
John Doe	Internal	CEO	High	High	Financial expertise	Budget	johndoe@madeup.com
Susan Sunshine	External	Client	High	High	Approves deliverables	Project timeline	susansunshine@madeup.com





Project charter

The project charter

- Reason for the project
- Main stakeholders
- Benefits of the project
- Objectives and constraints
- Risks identified
- Budget overview



Initiation Phase



**Scope of
the project**



Stakeholders



**Project
Charter**

