



Professional Diploma in

Project Management

Project Monitoring & Controlling



Define monitoring & controlling ◀

Examine the ten phases of monitoring & control ◀

Objectives

Lesson 7



Monitoring & controlling


Monitoring & controlling

Ensuring that project objectives are met by monitoring and measuring progress regularly to identify variances from the plan so that corrective action can be taken



Monitoring & controlling

- Main function of a project manager
- Will feature during the planning & execution phase of a project
- Can only be effective if applied throughout the process
- Can be useful to note points on the project plan

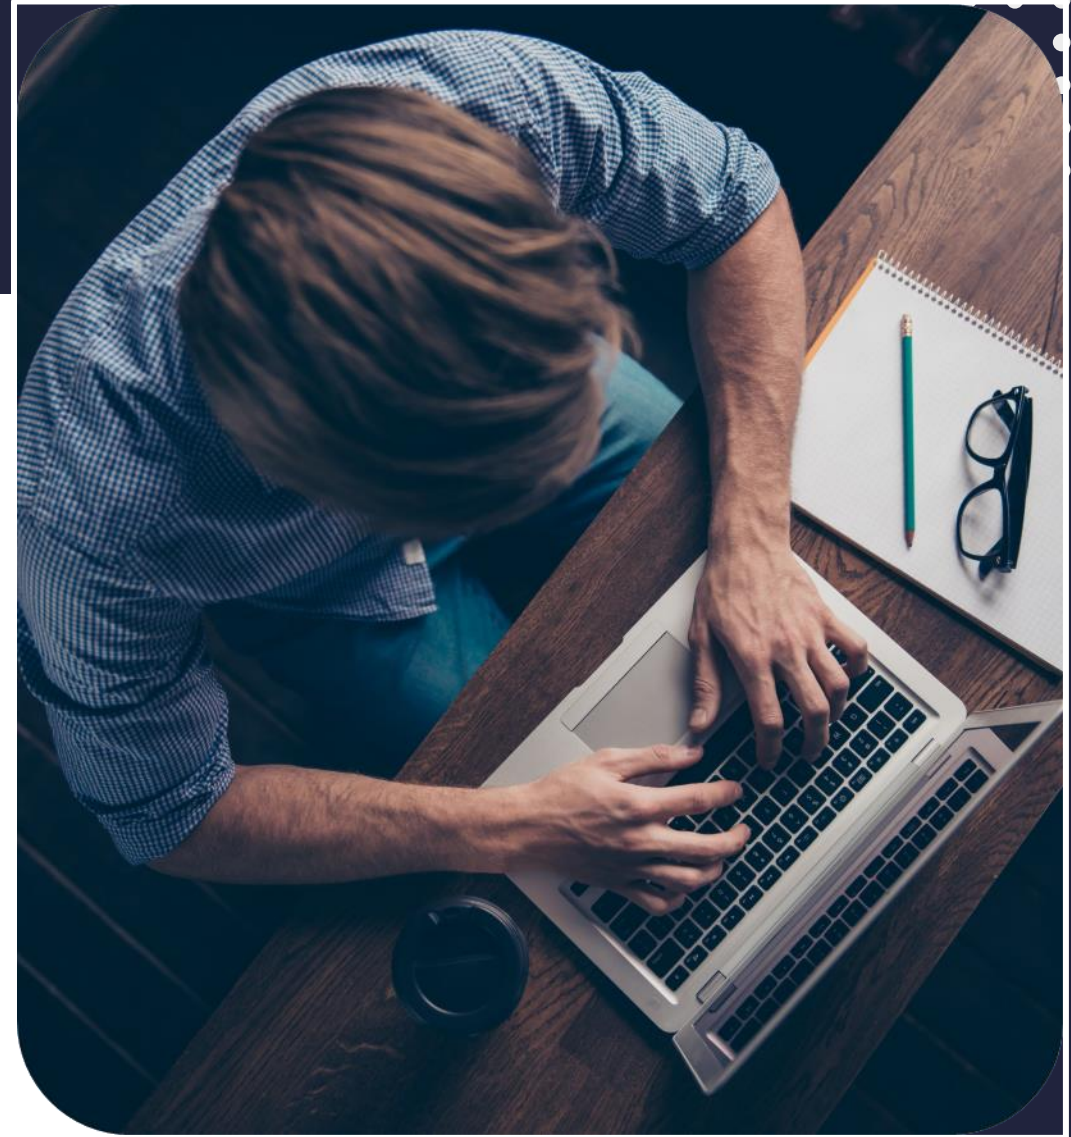



The ten steps of monitoring & controlling





1. Project work
2. Integrated change control
3. Scope verification
4. Scope control
5. Schedule control
6. Cost control
7. Quality control
8. Control risks
9. Performance reporting
10. Managing stakeholders



Project work


Recommended corrective actions

Recommended preventive actions

Forecasts

Recommended defect repair

Requested changes

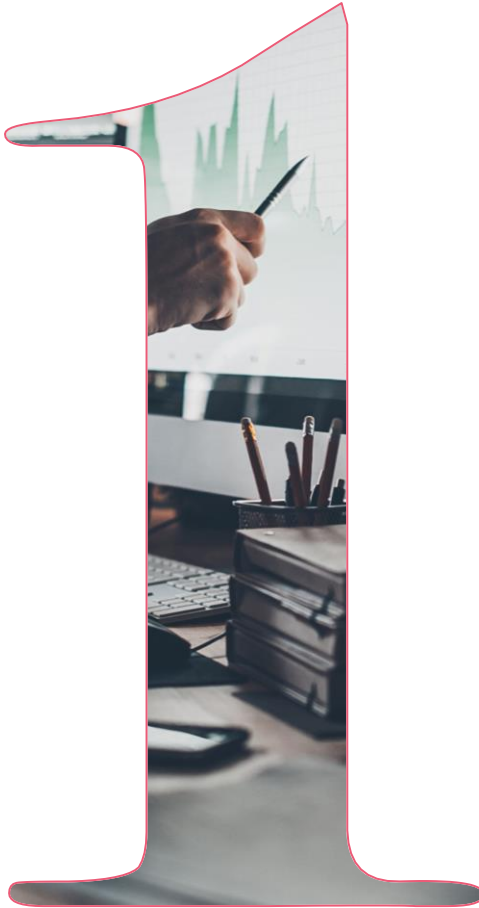



Integrated change control

Approved change requests

Rejected change requests

Updates to the Project Management Plan

Updates to the Project Scope Statement
(and requirements)





Scope verification

Re-evaluating:

The project plan

Project scope management plan

Work breakdown structure

Acceptance will be given






Scope control


Managing & controlling any changes

These changes will have been through the change control process & times/cost will have been estimated

It is important as a project manager to ensure the vital success factors are achieved

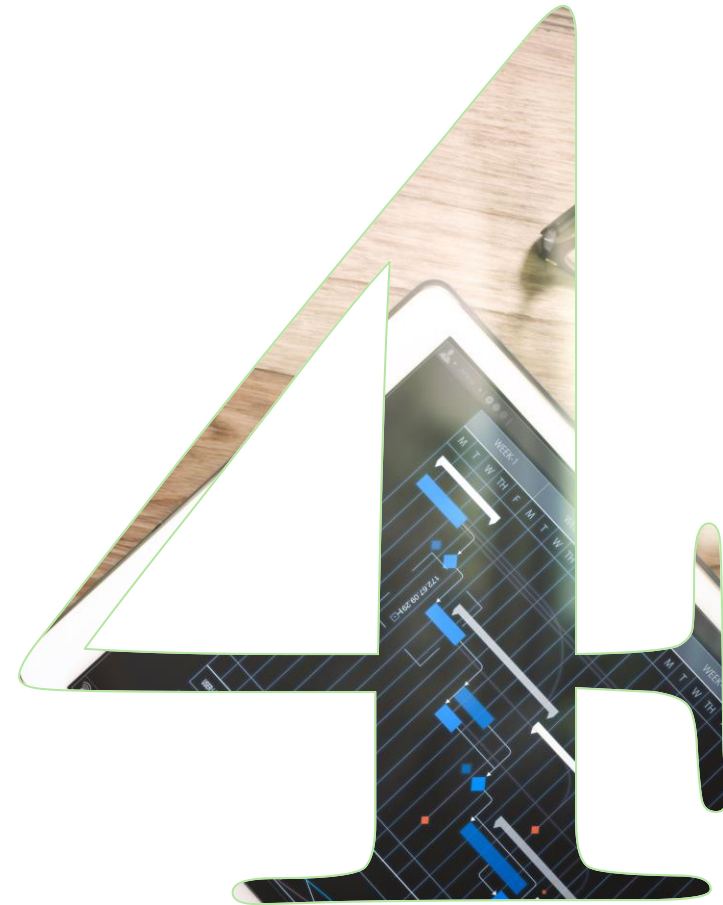

Scope Creep

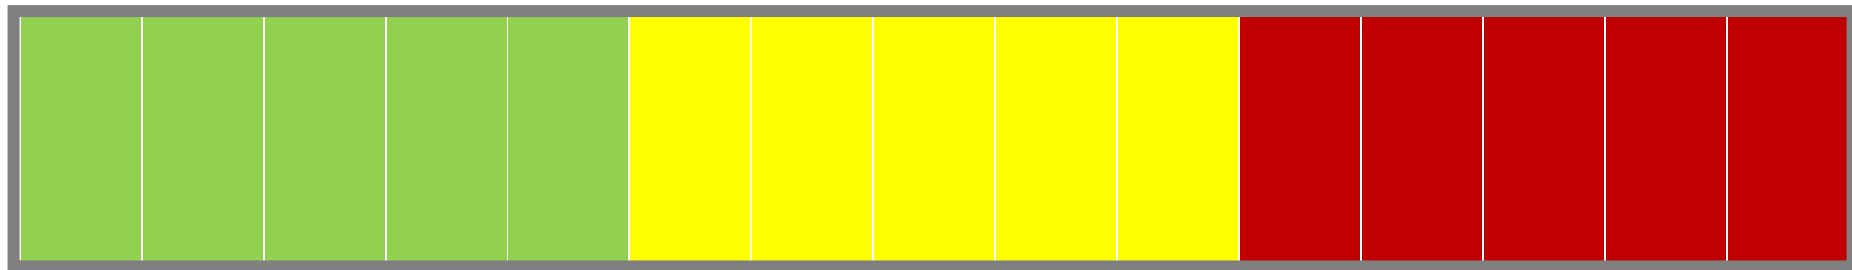

LOW

MEDIUM

HIGH



Schedule control

Aligning with project deadlines

Monitoring any changes, realised risks & task status (RAG)

The project baseline will be evaluated to establish if the project is on track

Reprioritisation of tasks, reviewing work progress, managing approved changes




+ Status meetings, reports & updates

- Update of project activities
- Evaluating project baseline
- Evaluate any potential risks
- Updates on budget & quality


This information once gathered and consolidated will be presented to key stakeholders



What do these diagrams represent?

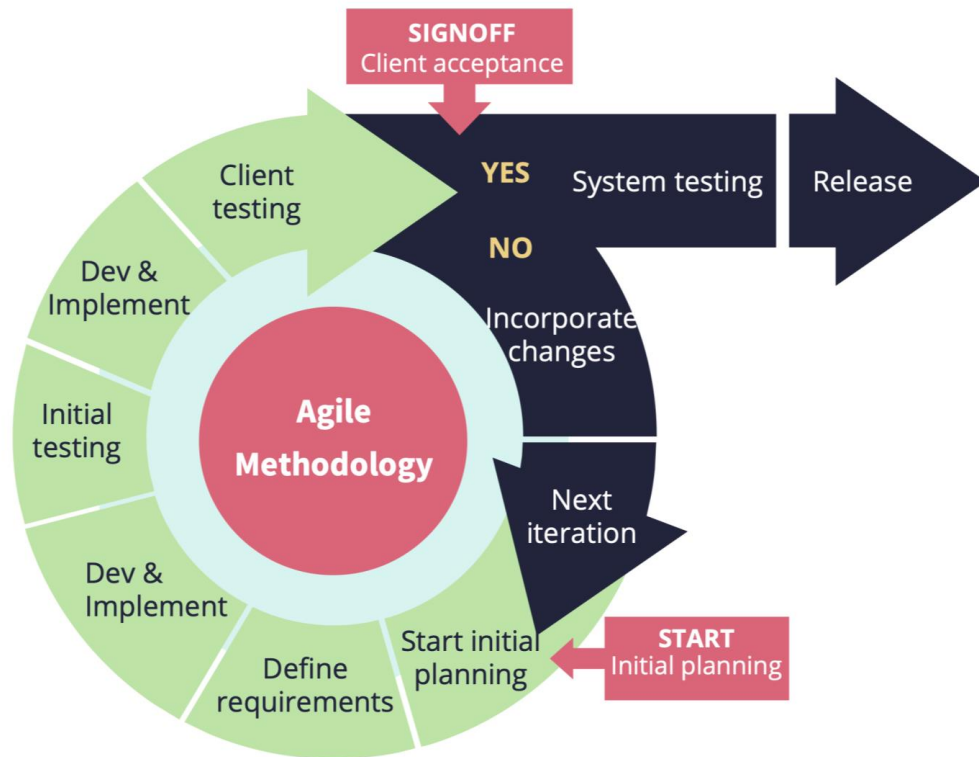

Waterfall Method

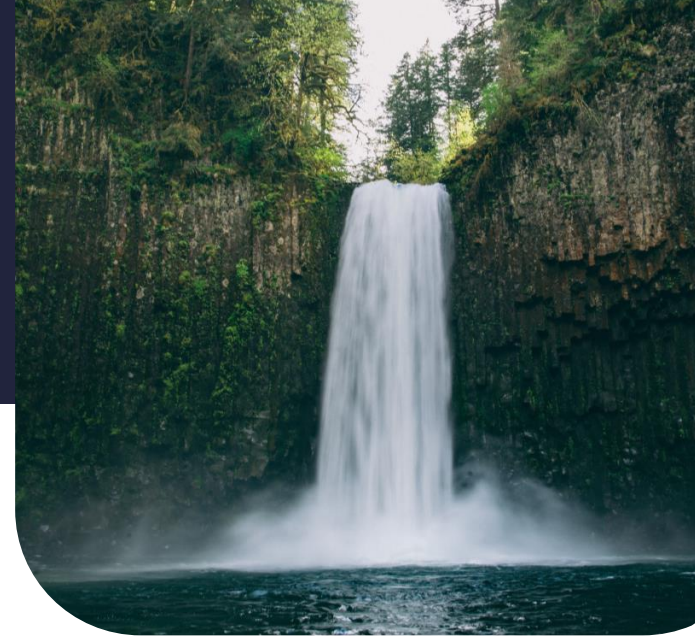

Design

Requirements


Implementation




Verification



Maintenance

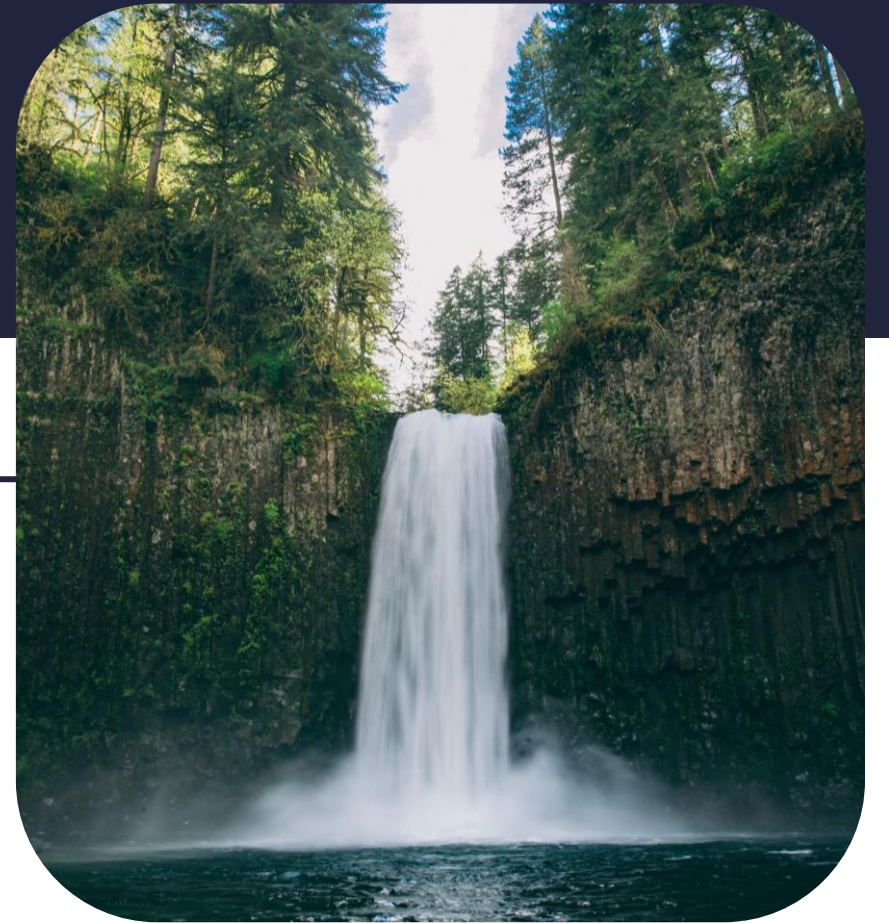

Agile Method

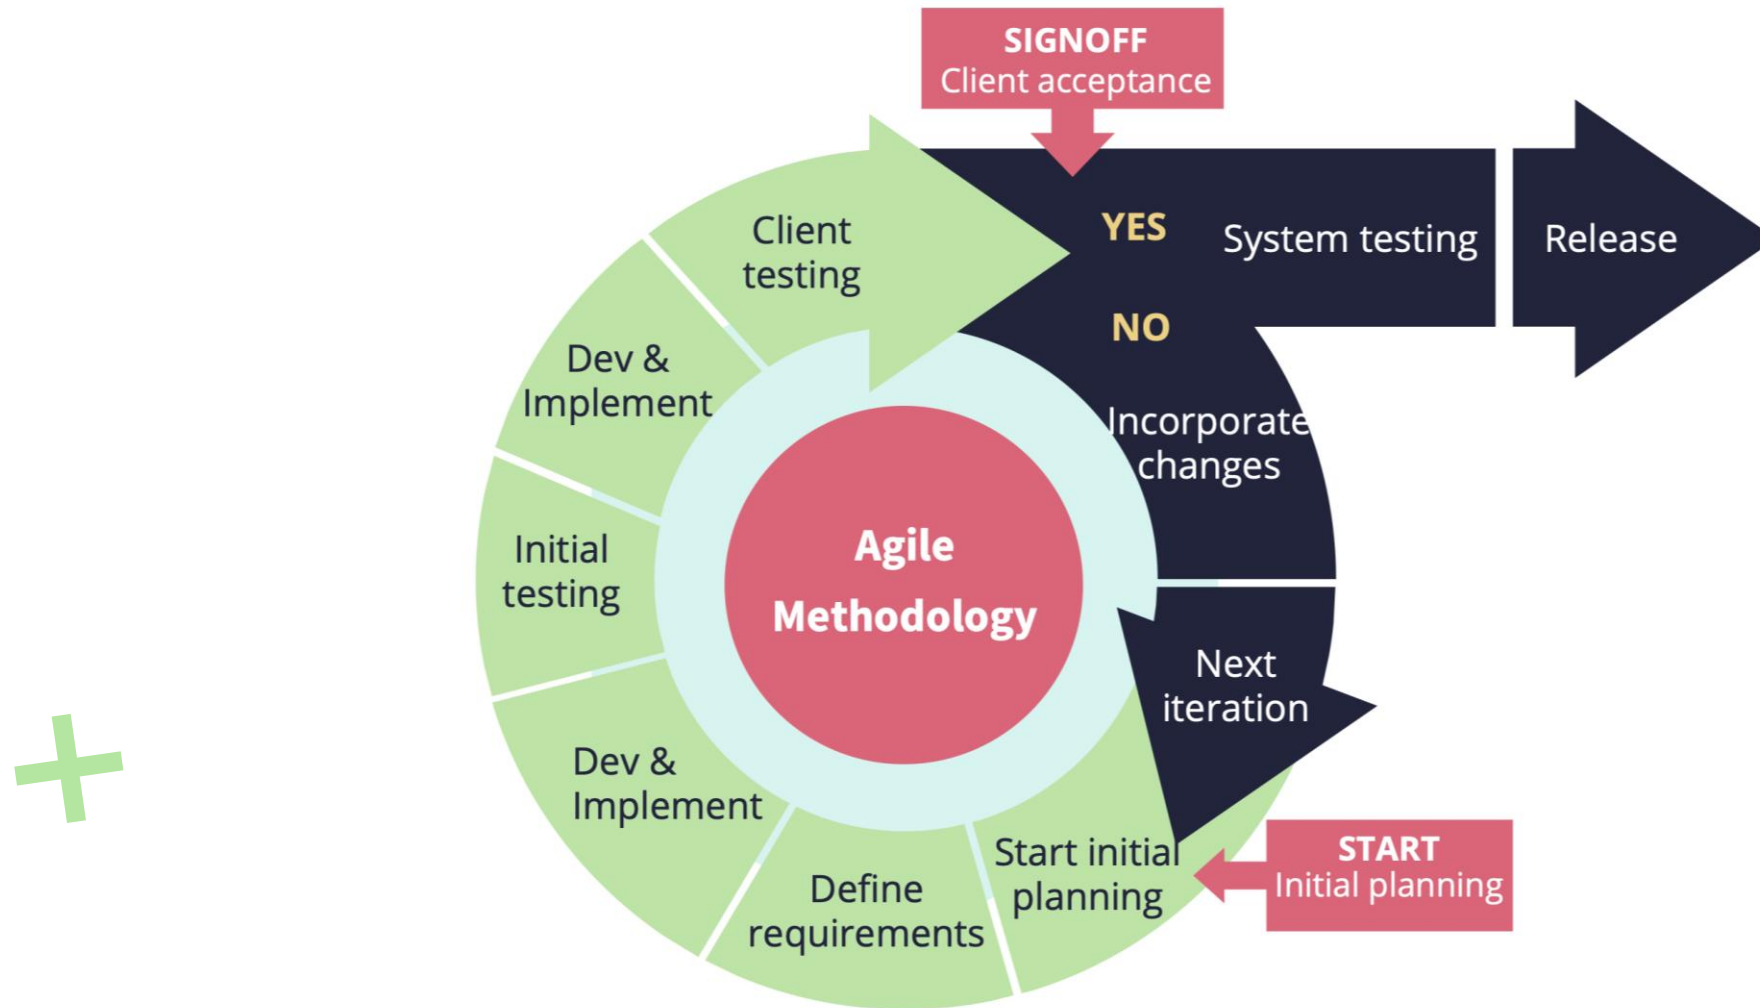



Cost control

Overseeing and managing the overall project budget

It allows opportunities to identify ways of reducing the expenses within the project

It also involves accounting for financial risks that could arise

If not controlled the project runs the risk of the project going over budget and not aligning with scope





Quality control

Validating the deliverables

Meeting the requirements as specified by the stakeholders

Identifying cause of poor product quality

Recommending necessary actions to eliminate problems related to quality





Control risk

Allows the project manager to respond to risks using strategies & contingency plans that have already been planned

This allows for fast action in terms of limiting the impact of the realised risk





Control risk

During this process, the following will be reviewed:

Effectiveness of risk responses

Monitoring of potential additional risks

Evaluate risk triggers





Performance reporting



A percentage of the work completed during the reporting period

The balance of the work to be completed

Costs incurred during the reporting period

The balance of funds & time available

Significant risks that have occurred or passed without occurring





Performance reporting



Variance analysis (schedule variance and cost variance)

Performance indexes (schedule performance index and cost performance index)

The forecasted time/funds needed to complete the remaining work

A summary of major approved change requests during the reporting period





Managing stakeholders

Engage stakeholders: Remember, it's better to overcommunicate than to assume that stakeholders are on the same page as you

Use your analysis of stakeholder influence/interest to achieve a good balance of interaction

Key stakeholders should be closely involved with business decisions, whereas other departments may require less involvement





Managing stakeholders

Gain feedback, refine approach:

- The biggest determining factors for effective stakeholder management are time and experience
- Follow the steps laid out above and ask for feedback from stakeholders. This can help you refine and perfect your approach

Coming up in Lesson 8...



Project closure

Things to consider when closing a project:

- Performance reporting
- Procurement closure
- Fund reallocation
- Project hand-off
- Releasing resources

Lessons learned explained

The completed project lifecycle



Challenge

Which of the 10 phases of monitoring do you think is the most important?

