



Professional Diploma in

Project Management

Lesson 8: Project Closure



**Did you
know?**

**57% of projects fail
due to a lack of
communication in
the project team.**





Project closeout activities <

Project closure report <

Lessons learned <

Objectives

Lesson 8

7 steps of project closeout



1. Deliverables completed
2. Client acceptance
3. Procurement closure
4. Resources release
5. Closure report
6. Lessons learned
7. Archive documents

Project closeout



Closeout timeframes




Deliverable completion

Phase completion

Iteration completion

Designated times



**Closeout practical
example: creating a
website for a client**



Deliverables completed

- When project is ready, client will be contacted for acceptance testing
- If not acceptable, next iteration will commence
- If satisfactory, client will formally accept deliverable





Client acceptance

- Customer agrees that the scope of the project and deliverables are complete and were delivered as agreed
- Formal acceptance (in writing)





Procurement closure

- Settle and close contract agreements
- Administrative duties such as finalising payments, updating records, and archiving information





Resources released

- Equipment and facilities to be re-assigned
- Staff moved on to other projects
- Release contingency funds






The closure report

Elements of a closure report



Project baseline vs deliverable completion



Project budget estimate vs actual budget



Predicted risk vs realised risk




Pre-defined scope vs scope changes

Components of a Closure report

- Summary statement
- Results and outcomes of the project
- Project scope, project schedule, and project budget
- Project performance analysis
- Challenges and risks
- Lessons learned
- Recommendations
- Conclusion






Closure report template

PROJECT INFORMATION

	DESCRIPTION
Project Name	
Project Description	
Project Manager	
Project Sponsor (Customer)	



Closure report template

VARIANCE TABLE

	BASELINE	ACTUAL	VARIANCE	% VARIANCE	COMMENTS
PROJECT SCHEDULE					
Start Date					
End Date					
PROJECT BUDGET					
Budget					



Closure report template

KEY RISKS

RISK DESCRIPTION	RESPONSE	RESULT	COMMENTS
Confidential information being leaked	Hire security firm to secure site as well as IT	No premises or system breaches	The potential losses justified the increased spend of outsourcing security



Lessons learned



Who attends a lessons learned session?

- Project team
- Stakeholders
- Executive management
- Maintenance and operations staff
- Project support staff



**Professional
tip**



**Schedule lesson
learned sessions
throughout the
project.**






**Were the goals
achieved and if
not, why?**



**Was the customer
satisfied with the
end product/s?**

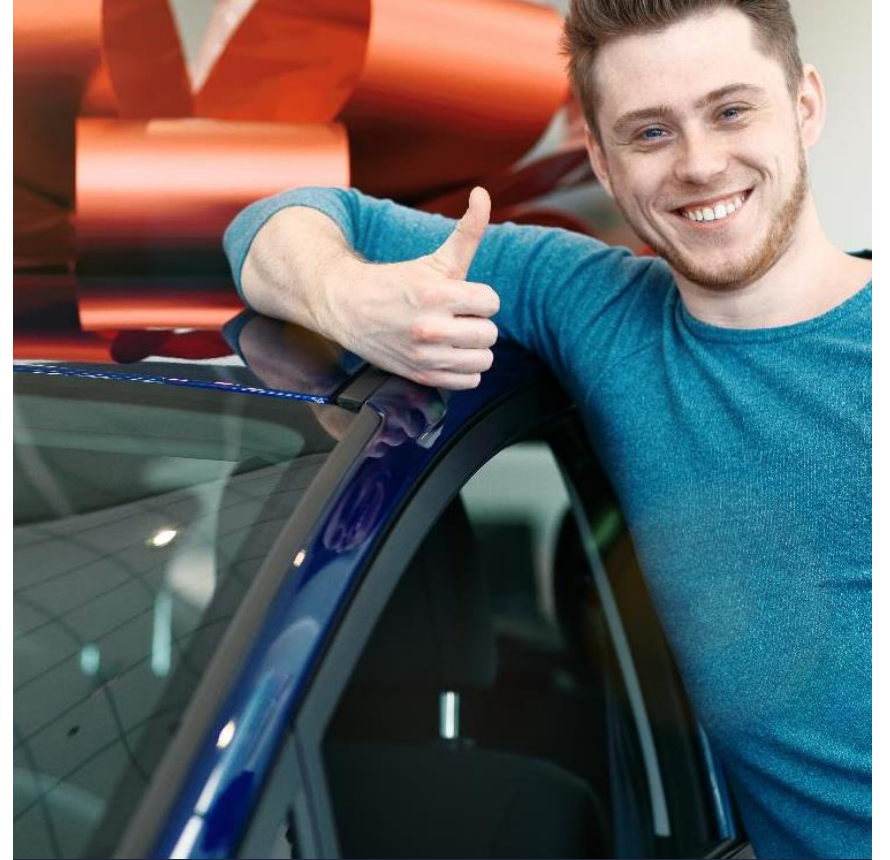

Project variables

Costs?

Schedule?

Risks?






Project methodology review

What went well?

What went wrong?

Where can improvements be made?



**Lessons learned should be
presented, openly discussed, and
documented.**



Lessons learned documentation tips

EXAMPLE TABLE

ID	EVENT	RAG	EARLY INDICATORS	SUGGESTED ACTION	LESSON LEARNED
1					
2					
3					

- Compile a questionnaire of open-ended questions
- Collate feedback into a table (using RAG status)
- Distribute the compiled document to all participants for review
- Compile a FAQ document for circulation



Archive records

- Documents no longer available (cannot be edited)
- Ensuring records are retrievable for future reference






To summarise...







The Project Management life cycle

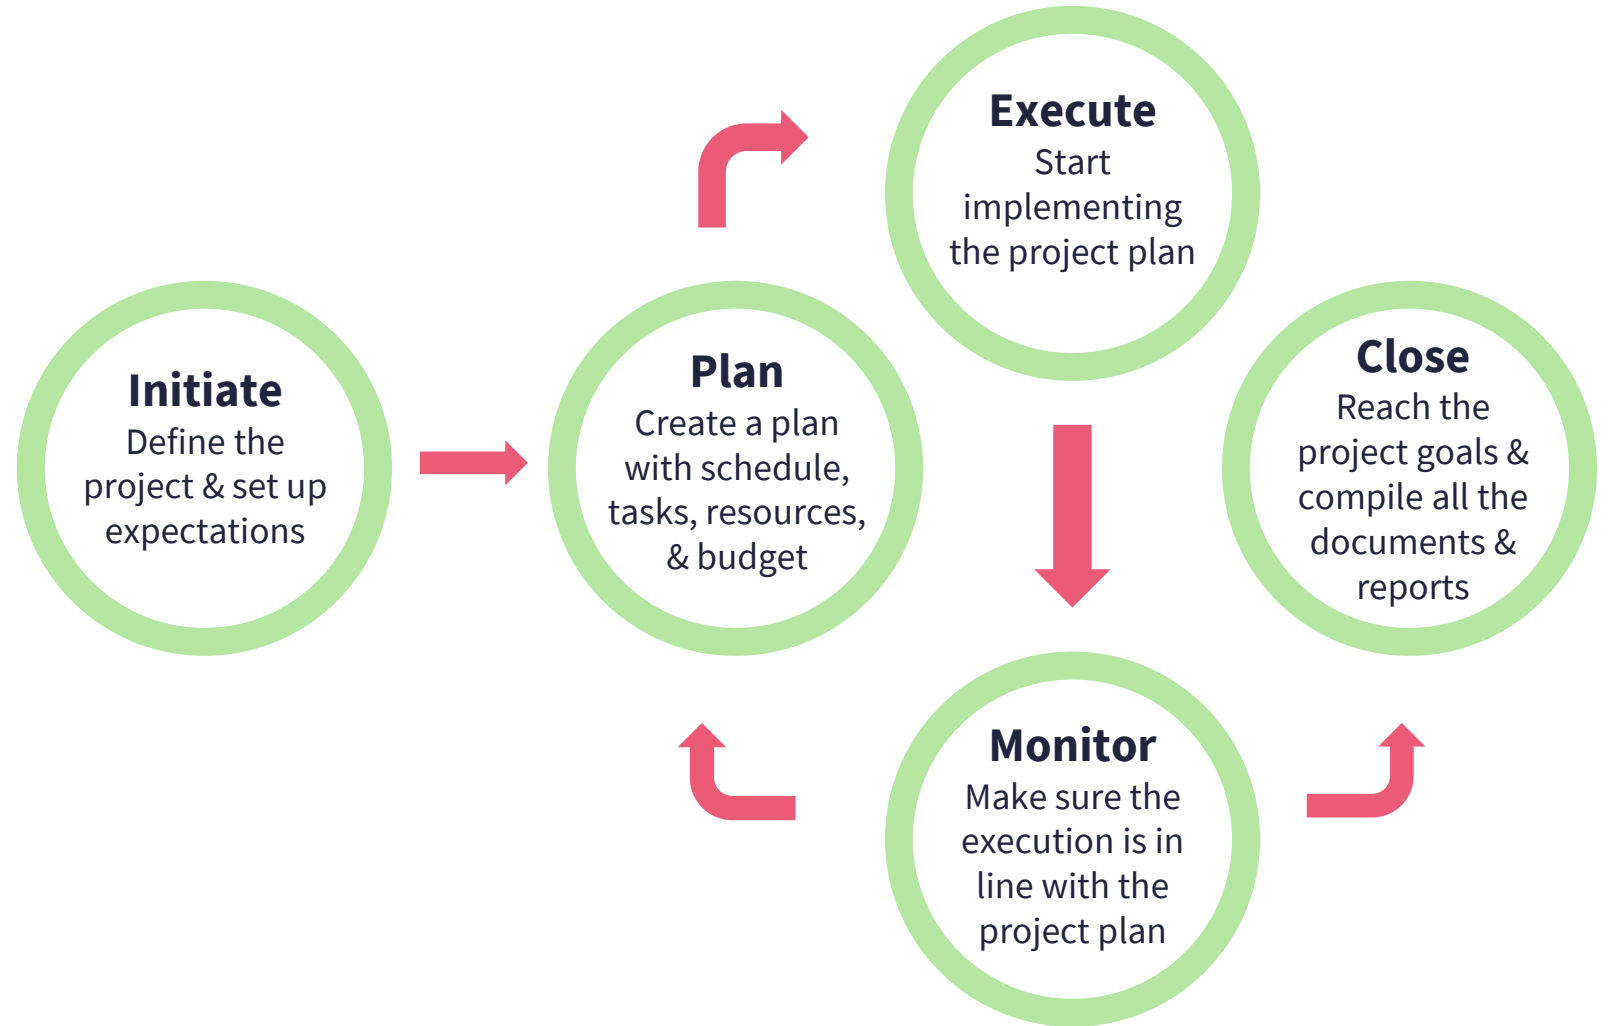

If project is not in line with plan...

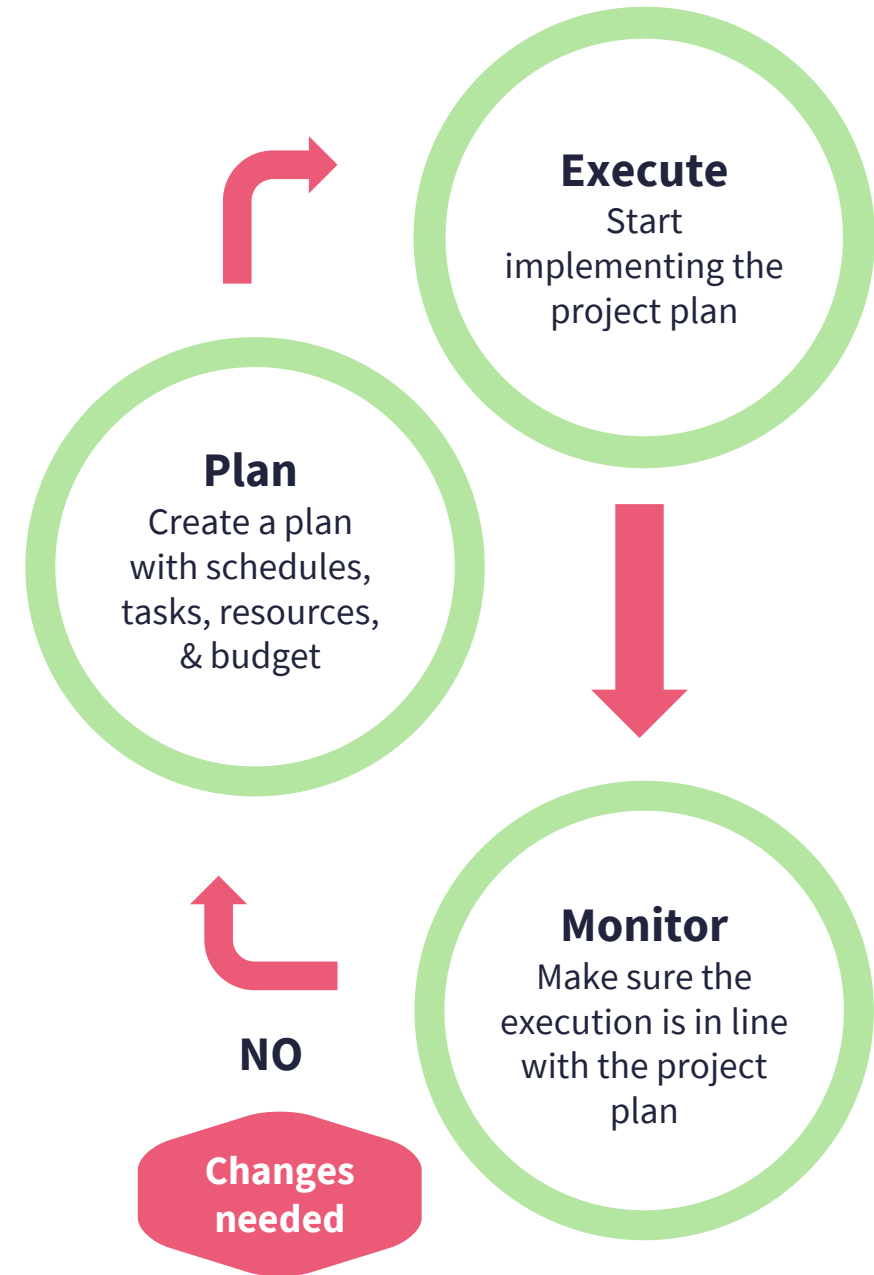

The Project Management lifecycle

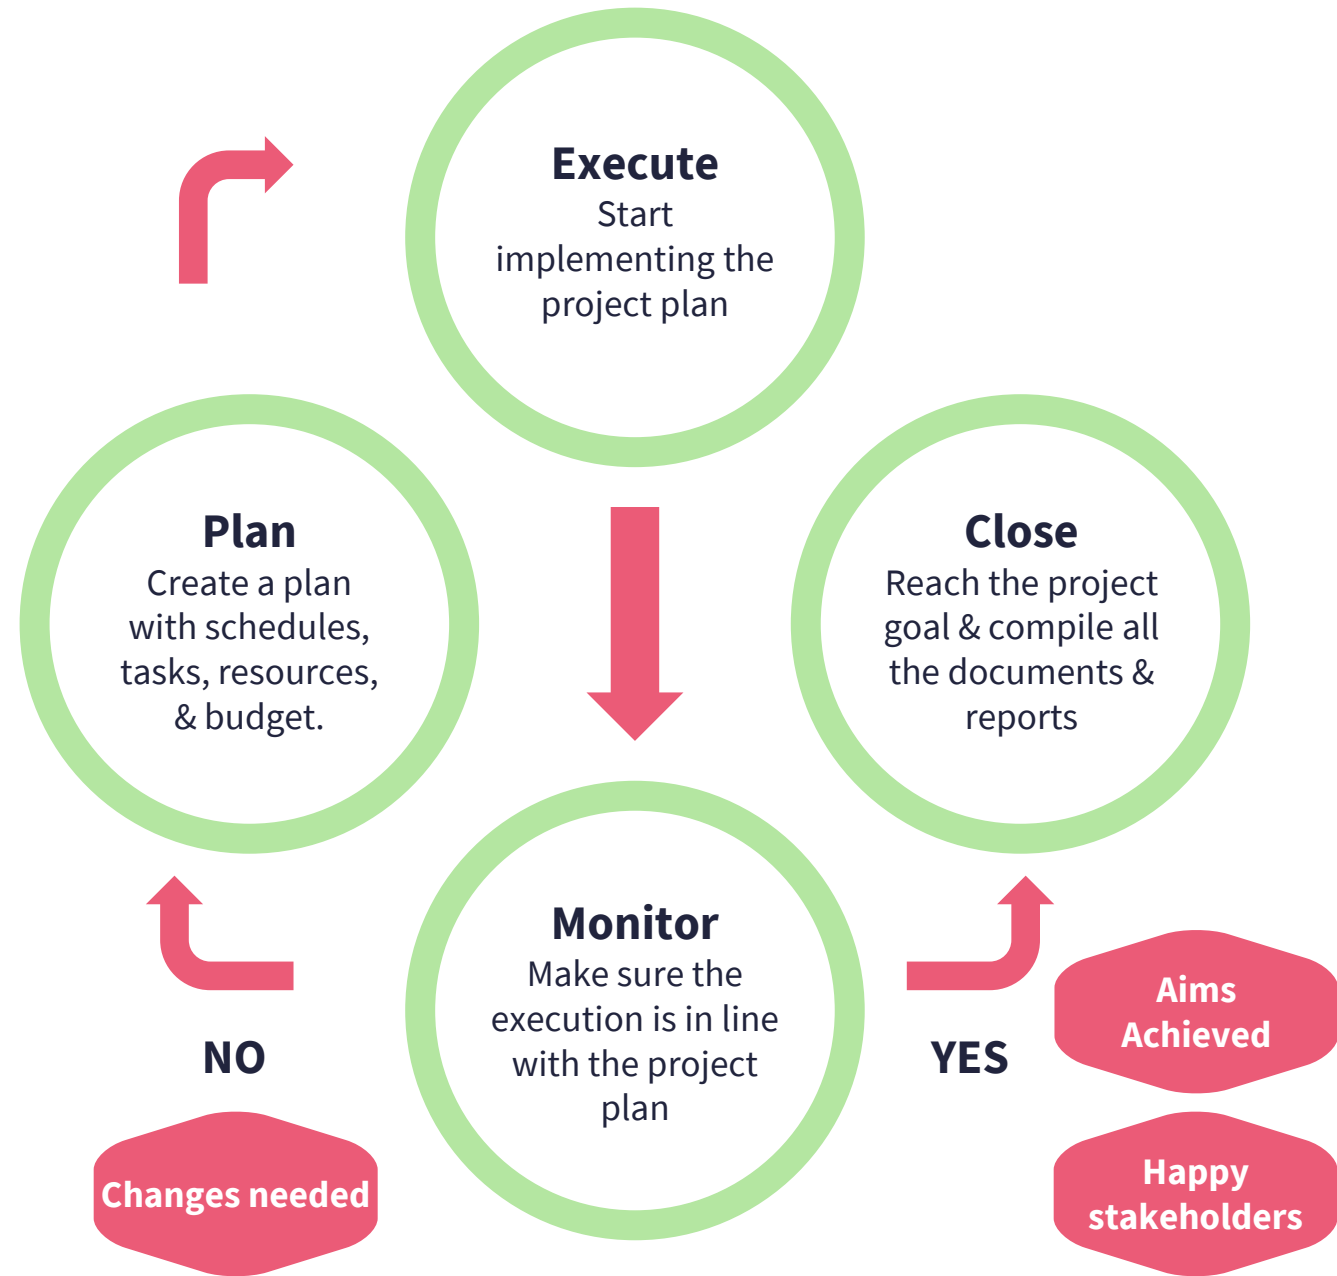



Congratulations!

**You have completed
Project Management!**

